

24 November 1971

CONSTRUCTION				MOVING						
SEC.	DATE		REMARKS	WORK DAYS	DATE		JOB	SECTION		*
	START	COMPLETE			FROM	TO		FROM	TO	
15-18				16	11/22/71	12/15/71	Prepare Boxes for Move			
9-10	10/18/71	12/15/71		8	12/27/71	1/ 6/72	3600 Boxes	15 & 16	9 & 10	P
				6	12/16/71	12/23/71	2800 Boxes	2	8	T
8	10/18/71	12/15/71	Rework	6	2/ 9/72	2/25/72	2500 Boxes	A-25	8	P
6	11/22/71	1/ 4/72	Rework	8	1/ 7/72	1/18/72	3600 Boxes	11 & 13	6	P
4	12/13/71	1/ 7/72	Rework	8	1/19/72	1/28/72	3600 Boxes	12 & 14	4	P
				6	2/ 1/72	2/ 8/72	2800 Boxes	8	2	P
2	12/27/71	1/31/72	Rework	6	2/ 9/72	2/25/72	2500 Boxes	A-25	8 & 2	P
19-22				8	2/28/72	3/ 8/72	Prepare Boxes for Move			
11	1/20/72	3/ 9/72		8	3/10/72	3/21/72	3600 Boxes	17 & 18	11	P
12	1/31/72	3/17/72		12	3/22/72	4/ 6/72	Bal. of	19-22	12	P
13	1/20/72	3/ 9/72					Wing C		13	
14	1/31/72	3/17/72								
7	2/ 1/72	3/ 7/72	Rework							
5	2/15/72	3/20/72	Rework							
				6	4/ 7/72	4/14/72	3000 Boxes	3	7	T
3	4/17/72	5/19/72	Rework							
				6	4/17/72	4/24/72	2800 Boxes	1	5	T
1	4/25/72	5/25/72	Rework							
				6	5/22/72	5/29/72	3000 Boxes	7	3	P
				6	5/30/72	6/ 6/72	2800 Boxes	5	1	P
15&16	1/ 7/72	2/25/72								
17&18	3/22/72	5/15/72								
19	3/27/72	5/15/72								
20	3/30/72	5/18/72								
21	4/ 4/72	5/24/72								
22	4/ 6/72	5/25/72								
Clean-Up		6/ 2/72								

* T - Temporary Location


P - Permanent Location

25X1A5a1

25X1A5a1

- NOTES: 1. The dates were added and/or changes from the schedule submitted by [REDACTED] dated 11/19/71, to conform to the availability of completed space and the ability of the Using Service to move boxes to and from this space.
2. The Using Service's original moving time has been reduced by 1/3 in an effort to cooperate with [REDACTED] in completing a quality job in the shortest possible time.
3. Moving dates will be adjusted as possible to meet any improvement in construction time.

Sanitized - Approved For Release :
CIA-RDP74-00005R000100060010-7

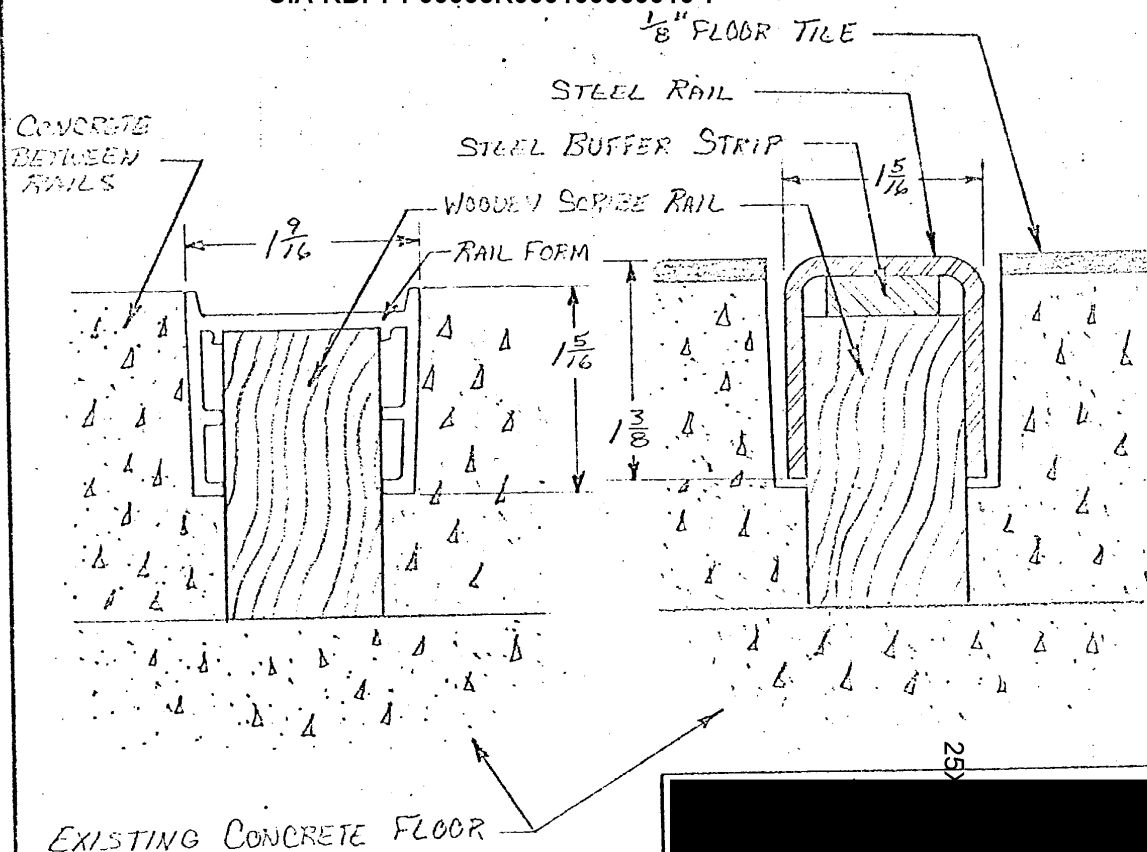

ADDED DIMENSIONS			
REV	DATE	BY	CKED
1	11/15/71	GMB	

IBM#				PLASTIC RAIL FORM (TYPICAL)			
DRAWN BY		DATE		ACCOUNT		SCALE	
G.M.B.		11/15/71		[REDACTED]		FULL	
CHECKED BY		DATE		EXP.-		DRG NO.	
		11/15/71					

Sanitized - Approved For Release :
CIA-RDP74-00005R000100060010-7

25X1A5a1




5 January 1972

25X1A1d




Re: Moveable Shelving, Bldg. A-18



25X1A6a

25X1A1d

On 19 November 1971 this office requested that a proposed extension of the completion date through 30 June 1972 by  be denied. 25X1A5a1

At that time an extension of the completion date through the end of the fiscal year would have reduced our bonding capacity at a very crucial time. Recently this circumstance has been resolved with the bonding company.

Please disregard the objection to an extension of the completion date beyond 7 April 1972.



Owner

25X1A5a1

C
O
P
Y
